

Course: Individual Software Development Process' 2026

Iteration Report: Iteration 1

By **sonnyboy**

Chosen Irl Challenge: Project Aj. Milk : Lab Workflow & Request Management



Pannathon Nithiwatcharin	6710545695
Krittin Konsiang	6510545241
Paramee Saejia	6710545709
Piyapong Ausawarachan	6710545725
Phubet Ueananta	6710545814

Table of Contents

1. Project Snapshot.....	1
1.1 Project-Wide Gantt Chart.....	1
1.2 Current Iteration Gantt Chart.....	1
2. Sprint/Board Status Snapshot.....	1
3. Scope Addition/Change Log.....	2
4. Retrospective.....	2
5. Testing & Quality Notes.....	2
6. Project Risk Register.....	3
7. Individual Contribution Log.....	3

1. Project Snapshot


Note: This section must include both Gantt Chart for the whole project and the calculation of the critical path for the project, and each iteration. Created via Plane.so.

Note: Project Repository is mandatory for the report submission of Iteration 2. For Iteration 1, this can leave blank as “(WIP)”.

Project Repository:

<https://github.com/Theme86/Sonny-boy-Lab-Workflow-Request-Management>


1.1 Project-Wide Gantt Chart

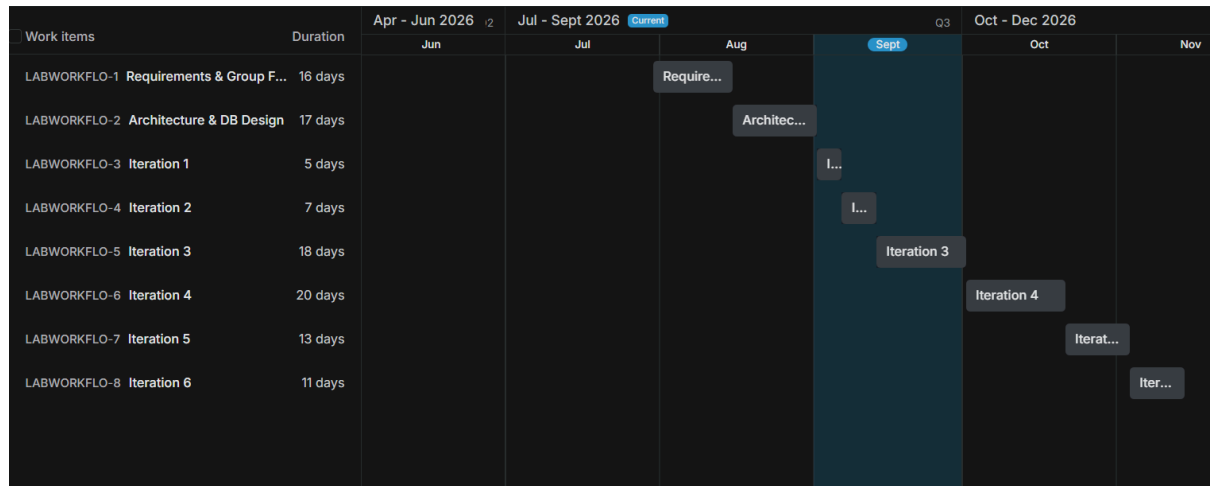

Critical Path: Requirements & SRS sign-off (done) → Architecture/DB schema finalisation (Docker + RDBMS) → Google OAuth / Auth Module (SRS-18, SRS-19) → Submit Request implementation (US-1) → Triage/Assign logic (US-3, needs both Auth and US-1) → Update Status & Close Request (US-4, US-5) → Dashboard (US-6, needs US-4/US-5 data to be meaningful) → Industry Collaboration + Restricted visibility (US-7, US-8 — needs the base request model and role system mature) → Role management (US-9, needed before restricted-access testing is fully verifiable) → Deployment

Critical Path Duration: 103-106 calendar days

1.2 Current Iteration Gantt Chart

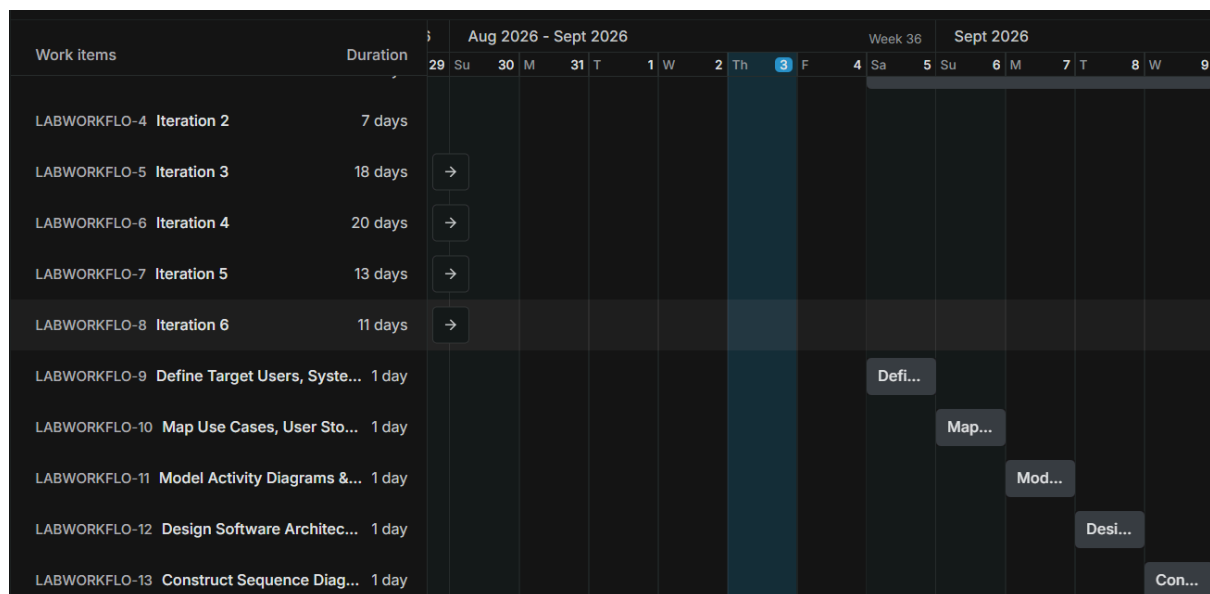

Critical Path: Define Target Users, System Goals & KAOS Goal Refinement → Map Use Cases, User Stories & User Requirements (URS) → Model Activity Diagrams & System Requirement Specifications (SRS) → Design Software Architecture, Storage & Dev Environment → Construct Sequence Diagrams & Traceability Matrix Review

Critical Path Duration: 5 days

2. Sprint/Board Status Snapshot

Note: User Stories Must Be Consistent User Stories in Software Proposal (Week 4). For Maximum Capacity, It Must Be:

- 3 User Stories for Iteration 1
- 4 User Stories for Iteration 2

Iteration Goal: For this iteration, the scope is to plan future tasks and define the direction of the project.

Capacity Declared: 0 user stories (at the Iteration 1 hard limit; no basis needed as this is the fixed ceiling for a first iteration).

User Story	Description	Owner	Status	Within Capacity (Y/N)	Notes
-	-	-	-	-	-

3. Scope Addition/Change Log

Note: Log any item added, expanded, or swapped in after planning began. Empty is a good sign; frequent entries signal scope creep.

Item added/changed	Reason	What as dropped to compensate (one-in-one-out)

(None applicable)	Team stayed within the originally committed 0 user stories for the full iteration	(None)
-------------------	---	--------

4. Retrospective

What went well	What didn't go well	Action items for next sprint
The scope of work and timeline for future activities have already been defined and planned.	-	Design Software Architecture, Define the database schema and set up the initial database. , Auth Module (Google OAuth) implementation

5. Testing & Quality Notes

Note: any bugs, defects, tests (informal & formal) encountered and/or fixed during this iteration can be included here. If there is none, just put "(None applicable)" below.

None applicable was performed on this Iteration.

6. Project Risk Register

Risk ID	Description	Likelihood (L/M/H)	Impact (L/M/H)	Mitigation/Contingency	Status
R-01	No experiences	H	H	-	Monitoring

7. Individual Contribution Log

Note: One row per member, filled in by that member. The submission of this file considered that the form below is consented and confirmed by the whole team. This section directly supports the Individual Project Contribution and Peer Evaluation grading components.

Note 2: For Iteration 1, evidence can be a reference to the video presentation/iteration report that is related to the responsible task(s) (e.g. Lalita's Evidence). However, for Iteration 2, the reference must be on **GitHub file and commit only**, which is uploaded by that team member.

Student Name	Tasks owned this sprint	Course concept(s) applied	Evidence	Self-rated effort (1-5)
--------------	-------------------------	---------------------------	----------	-------------------------

Krittin Kongsiang	Manage the google doc, Create Repository	Project Management	Iteration report, github repository	4
Paramee Saejia	Prepare the proposal and define the project scope.	Project Management	Iteration report	4
Piyapong Ausawarachan	Research and define the project scope	Project Management	Iteration report, Presentation	5
Phubet Ueananta	Help preparing documentation, proposal, presentation slide	Project Management	proposal, presentation slide	5
Pannathon Nithiwatcharin	Prepare the proposal and define the project scope.	Project Management	Iteration report	5
